

AFFKMS-Project Plan_v5.1(Amila)

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Work Complete	Remaining Duration	Jan 11, '15			
										S	M	T	W
1		AFFKMS Plan	112 hrs?	Mon 1/12/15	Fri 1/30/15			9%	99.3 hrs?				
2		DMS - Document Management System	138 hrs?	Thu 1/29/15	Mon 2/23/15		Amila	9%	122.35 hrs?				
3		Implement User Folders grid section	60.5 hrs	Thu 1/29/15	Mon 2/9/15		Amila	19%	45.25 hrs				
4		Tree Detail View	30 hrs	Thu 1/29/15	Tue 2/3/15		Amila	50%	15 hrs				
5		List all the folder and files inside a particular folder when clicked on the tree	15 hrs	Thu 1/29/15	Fri 1/30/15		Amila	50%	7.5 hrs				
6		When a folder is clicked it should display the contents inside it	15 hrs	Mon 2/2/15	Tue 2/3/15	5	Amila	50%	7.5 hrs				
7		Tab function for a document	29.5 hrs	Tue 2/3/15	Mon 2/9/15			0%	29.5 hrs				
8		Properties tab	5 hrs	Tue 2/3/15	Wed 2/4/15		Amila	0%	5 hrs				
9		Assigning Keywords	5 hrs	Tue 2/3/15	Wed 2/4/15	6	Amila	0%	5 hrs				
10		Preview Tab	24.5 hrs	Wed 2/4/15	Mon 2/9/15		Amila	0%	24.5 hrs				
11		R & D - have to check with various JavaScript libraries ,most of them don't support word	16 hrs	Wed 2/4/15	Fri 2/6/15	9	Amila	0%	16 hrs				
12		Implementation	0 hrs	Fri 2/6/15	Fri 2/6/15	11	Amila	0%	0 hrs				
13		WEEK ONE 15% BUFFER	8.5 hrs	Fri 2/6/15	Mon 2/9/15	12		0%	8.5 hrs				
14		Folder Tree	5 hrs	Fri 2/6/15	Mon 2/9/15		Amila	0%	5 hrs				
15		Stop Reloading the entire tree	5 hrs	Fri 2/6/15	Mon 2/9/15	12	Amila	0%	5 hrs				
16		Document Bulk Upload	63 hrs?	Mon 2/9/15	Thu 2/19/15		Amila	0%	63 hrs?				
17		R & D	12 hrs?	Mon 2/9/15	Tue 2/10/15	15	Amila	0%	12 hrs?				
18		Implementation of the use case	30 hrs	Tue 2/10/15	Mon 2/16/15		Amila	0%	30 hrs				
19		Ajax Uploads	8 hrs	Tue 2/10/15	Wed 2/11/15	17	Amila	0%	8 hrs				
20		Backend to support multiple uploads at once	16 hrs	Wed 2/11/15	Fri 2/13/15	19	Amila	0%	16 hrs				
21		WEEK TWO 15% BUFFER	6 hrs	Fri 2/13/15	Mon 2/16/15	20		0%	6 hrs				
22		UI implementation for the use case	3 hrs	Mon 2/16/15	Mon 2/16/15		Amila	0%	3 hrs				
23		Query Front end	3 hrs	Mon 2/16/15	Mon 2/16/15	21	Amila	0%	3 hrs				
24		Exception Handling for the use case	18 hrs	Mon 2/16/15	Thu 2/19/15		Amila	0%	18 hrs				
25		Handling upload types	3 hrs	Mon 2/16/15	Tue 2/17/15	23	Amila	0%	3 hrs				
26		Handling connection failures	3 hrs	Tue 2/17/15	Tue 2/17/15	25	Amila	0%	3 hrs				
27		Handling Performance and memory allocation for large	4 hrs	Tue 2/17/15	Wed 2/18/15	26	Amila	0%	4 hrs				







Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

























AFFKMS-Project Plan_v5.1(Amila)

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Work Complete	Remaining Duration	Jan 11, '15			
										S	M	T	W
28		Listing of files that have been uploaded in bulk, prompt	8 hrs	Wed 2/18/15	Thu 2/19/15 27		Amila	0%	8 hrs				
29		Checking Checkout with exception case validations	58 hrs?	Thu 2/19/15	Mon 3/2/15		Amila	0%	58 hrs?				
30		R & D & POC - For checking if the documents that are check	15 hrs	Thu 2/19/15	Fri 2/20/15 28		Amila	0%	15 hrs				
31		WEEK THREE 15% BUFFER	6 hrs	Fri 2/20/15	Mon 2/23/15 30			0%	6 hrs				
32		Study the implementation of the Current System	15 hrs	Mon 2/23/15	Wed 2/25/15 31		Amila	0%	15 hrs				
33		Implementation of the use case	22 hrs?	Wed 2/25/15	Mon 3/2/15		Amila	0%	22 hrs?				
34		UI implementation for the use case	8 hrs?	Wed 2/25/15	Thu 2/26/15 32		Amila	0%	8 hrs?				
35		Exception Handling for the use case	8 hrs?	Thu 2/26/15	Fri 2/27/15 34		Amila	0%	8 hrs?				
36		WEEK FOUR 15% BUFFER	6 hrs	Fri 2/27/15	Mon 3/2/15 35			0%	6 hrs				
37		Download previous versions of the document.	10 hrs	Mon 3/2/15	Tue 3/3/15		Amila	0%	10 hrs				
38		Study the implementation of the Current System	2 hrs	Mon 3/2/15	Mon 3/2/15 36		Amila	0%	2 hrs				
39		Implementation of the use case	4 hrs	Mon 3/2/15	Tue 3/3/15 38		Amila	0%	4 hrs				
40		UI implementation for the use case	2 hrs	Tue 3/3/15	Tue 3/3/15 39		Amila	0%	2 hrs				
41		Exception Handling for the use case	2 hrs	Tue 3/3/15	Tue 3/3/15 40		Amila	0%	2 hrs				
42		Show deleted folders / documents inside recycle bin as in AFFKMS1 if applicable - *	22 hrs	Tue 3/3/15	Fri 3/6/15		Amila	0%	22 hrs				
43		Study the implementation of the Current System	6 hrs	Tue 3/3/15	Wed 3/4/15 41		Amila	0%	6 hrs				
44		Implementation of the use case	6 hrs	Wed 3/4/15	Thu 3/5/15 43		Amila	0%	6 hrs				
45		UI implementation for the use case	2 hrs	Thu 3/5/15	Thu 3/5/15 44		Amila	0%	2 hrs				
46		Exception Handling for the use case	2 hrs	Thu 3/5/15	Thu 3/5/15 45		Amila	0%	2 hrs				
47		WEEK FIVE 15% BUFFER	6 hrs	Thu 3/5/15	Fri 3/6/15 46			0%	6 hrs				
48		Add Document from Template - **	24 hrs	Fri 3/6/15	Wed 3/11/15		Amila	81%	6 hrs				
49		Study the implementation of the Current System	4 hrs	Fri 3/6/15	Fri 3/6/15 47		Amila	75%	1 hr				
50		Implementation of the use case	8 hrs	Fri 3/6/15	Mon 3/9/15 49		Amila	75%	2 hrs				
51		UI implementation for the use case	8 hrs	Mon 3/9/15	Tue 3/10/15 50		Amila	75%	2 hrs				
52		Exception Handling for the use case	8 hrs	Tue 3/10/15	Wed 3/11/15 51		Amila	75%	2 hrs				
53		Other DMS Features	72 hrs?	Wed 3/11/15	Tue 3/24/15		Amila	0%	72 hrs?				
54		Ajax Document Uploads	12 hrs	Wed 3/11/15	Thu 3/12/15 52		Amila	0%	12 hrs				
55		WEEK SIX 15% BUFFER	6 hrs	Thu 3/12/15	Fri 3/13/15 54			0%	6 hrs				
56		Document Drag and Drop Upload	16 hrs	Fri 3/13/15	Tue 3/17/15 55		Amila	0%	16 hrs				
57		Non-Functional Requirements	8 hrs?	Tue 3/17/15	Wed 3/18/15 56		Amila	0%	8 hrs?				


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

AFFKMS-Project Plan_v5.1(Amila)

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	% Work Complete	Remaining Duration	Jan 11, '15				
58			Historical Events capturing with AOP	8 hrs	Wed 3/18/15	Thu 3/19/15	57	Amila	0%	8 hrs		S	M	T	W
59			WEEK SEVEN 15% BUFFER	6 hrs	Thu 3/19/15	Fri 3/20/15	58	Amila	0%	6 hrs					
60			Documents meta data capture	8 hrs?	Fri 3/20/15	Mon 3/23/15	59	Amila	0%	8 hrs?					
61			Document Root Split	8 hrs?	Mon 3/23/15	Tue 3/24/15	60	Amila	0%	8 hrs?					


Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

AFFKMS-Project Plan_v5.1(Amila)

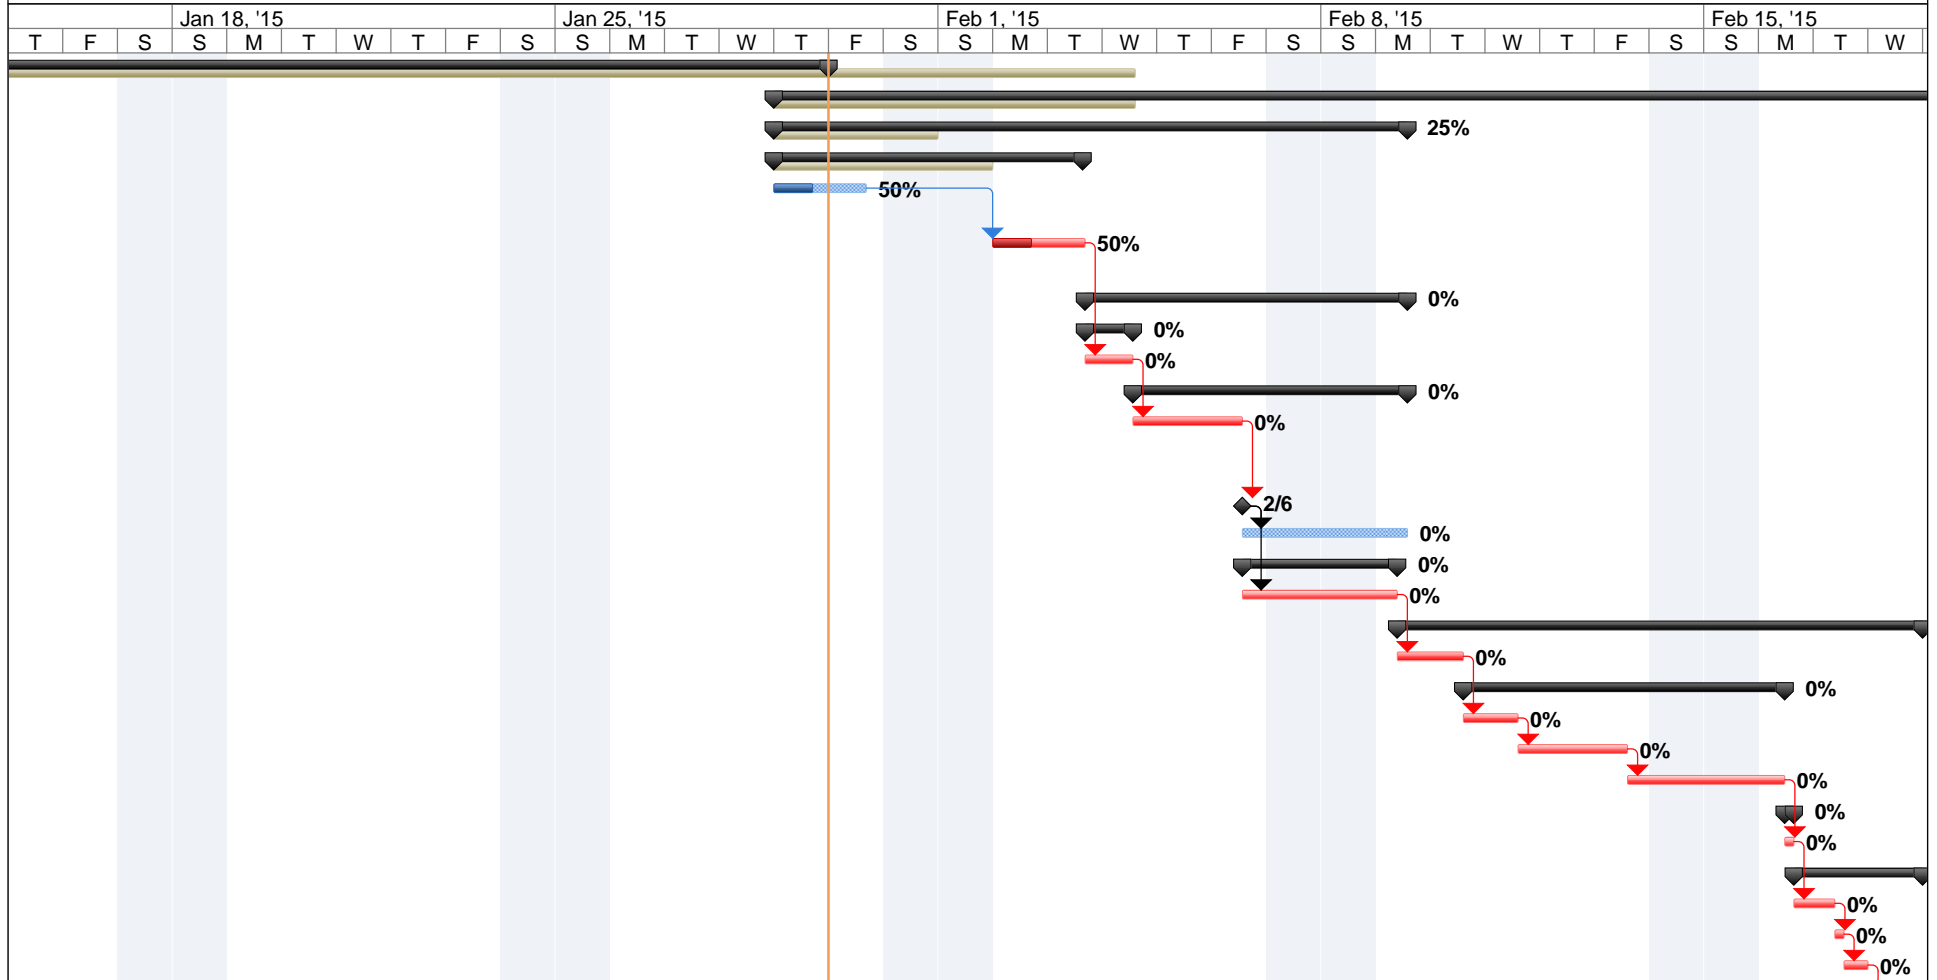

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	


AFFKMS-Project Plan_v5.1(Amila)

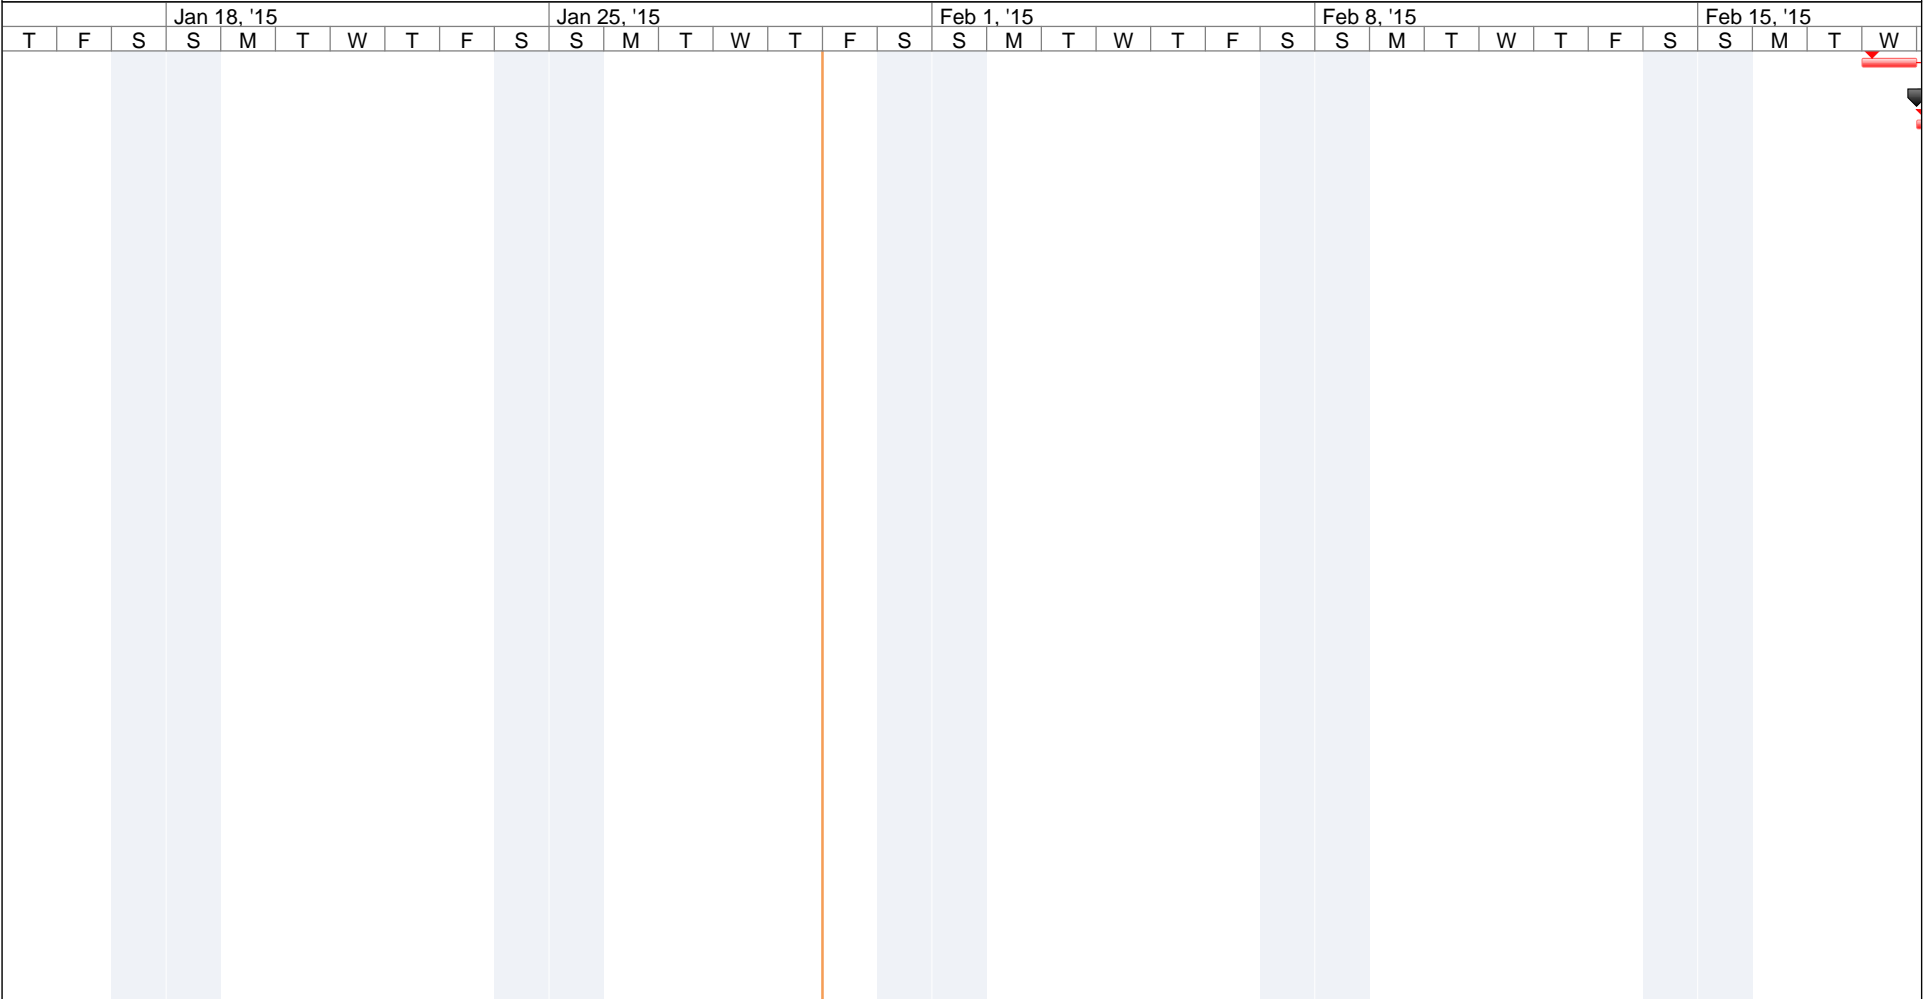

Critical	<div></div>	Finish-only	<div></div>	Manual Summary	<div></div>
Critical Split	<div></div>	Duration-only	<div></div>	Project Summary	<div></div>
Critical Progress	<div></div>	Baseline	<div></div>	External Tasks	<div></div>
Task	<div></div>	Baseline Split	<div></div>	External Milestone	<div></div>
Split	<div></div>	Baseline Milestone	<div></div>	Inactive Task	<div></div>
Task Progress	<div></div>	Milestone	<div></div>	Inactive Milestone	<div></div>
Manual Task	<div></div>	Summary Progress	<div></div>	Inactive Summary	<div></div>
Start-only	<div></div>	Summary	<div></div>	Deadline	<div></div>


AFFKMS-Project Plan_v5.1(Amila)

			Jan 18, '15							Jan 25, '15							Feb 1, '15							Feb 8, '15							Feb 15, '15			
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W



Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

AFFKMS-Project Plan_v5.1(Amila)

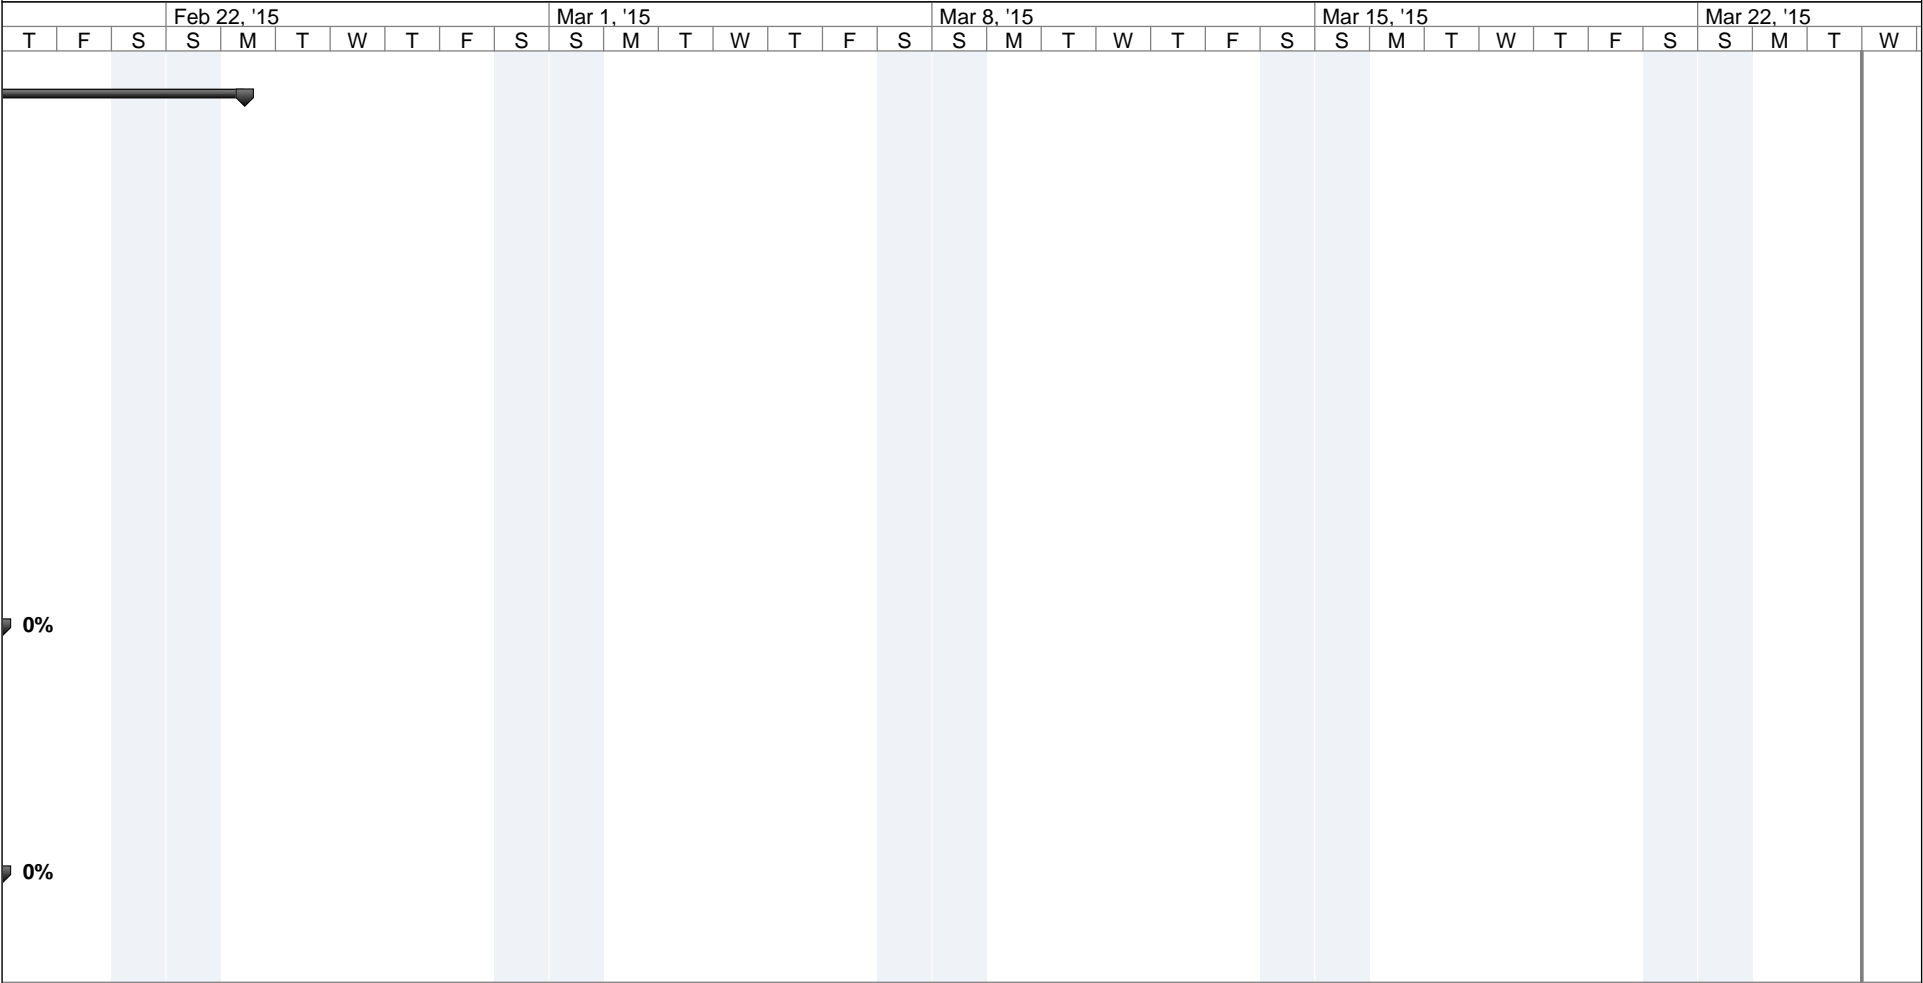

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

AFFKMS-Project Plan_v5.1(Amila)

The Gantt chart displays the project schedule for AFFKMS-Project Plan_v5.1(Amila). The timeline spans from February 22, 2015, to March 22, 2015. The chart shows a series of tasks and milestones, with progress bars indicating completion status. Key tasks include 'Critical', 'Task', 'Manual Task', and 'Start-only'. Milestones are marked with diamonds. The chart also includes a legend for various symbols and colors used in the project plan.

Task	Start Date	End Date	Progress
Critical	Feb 22, '15	Mar 1, '15	0%
Task	Mar 1, '15	Mar 8, '15	0%
Manual Task	Mar 8, '15	Mar 15, '15	75%
Start-only	Mar 15, '15	Mar 22, '15	0%

Legend:

- Critical: Red solid bar
- Task: Blue solid bar
- Manual Task: Green solid bar
- Start-only: Black solid bar
- Finish-only: Red dashed bar
- Duration-only: Blue dashed bar
- Baseline: Grey solid bar
- Baseline Split: Grey dashed bar
- Baseline Milestone: Grey diamond
- Milestone: Black diamond
- Summary Progress: Green solid bar
- Summary: Black solid bar
- Manual Summary: Red solid bar
- Project Summary: Blue solid bar
- External Tasks: Grey solid bar
- External Milestone: Grey diamond
- Inactive Task: Grey solid bar
- Inactive Milestone: Grey diamond
- Inactive Summary: Grey solid bar
- Deadline: Green arrow

[illegible]
